



# Arlington High School Building Project

AHS Construction Update – 8/18/2022

## Arlington HS Construction Schedule: April 2020 – April 2025

### Construction Details

Phase 1 construction is complete and the new Performing Arts and Science, Technology, Engineering, Arts & Mathematics wings are open. For Phase 1, only final testing and landscape work remains. Phase 2 began immediately after the Phase 1 building turnover. Part of the old school has been demolished and that area is closed off from the existing school during the next phase of construction.

### COVID-19 Update


The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly Construction Updates  
<https://ahsbuilding.org/news/construction-updates/>  
 For more information, visit:  
[www.ahsbuilding.org](http://www.ahsbuilding.org)  
 Email questions or concerns to:  
[ahsbuilding@arlington.k12.ma.us](mailto:ahsbuilding@arlington.k12.ma.us)

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative,  
 (617) 352-8593



### PHASE 2 BUILDING CONSTRUCTION (February 2022 – September 2023)

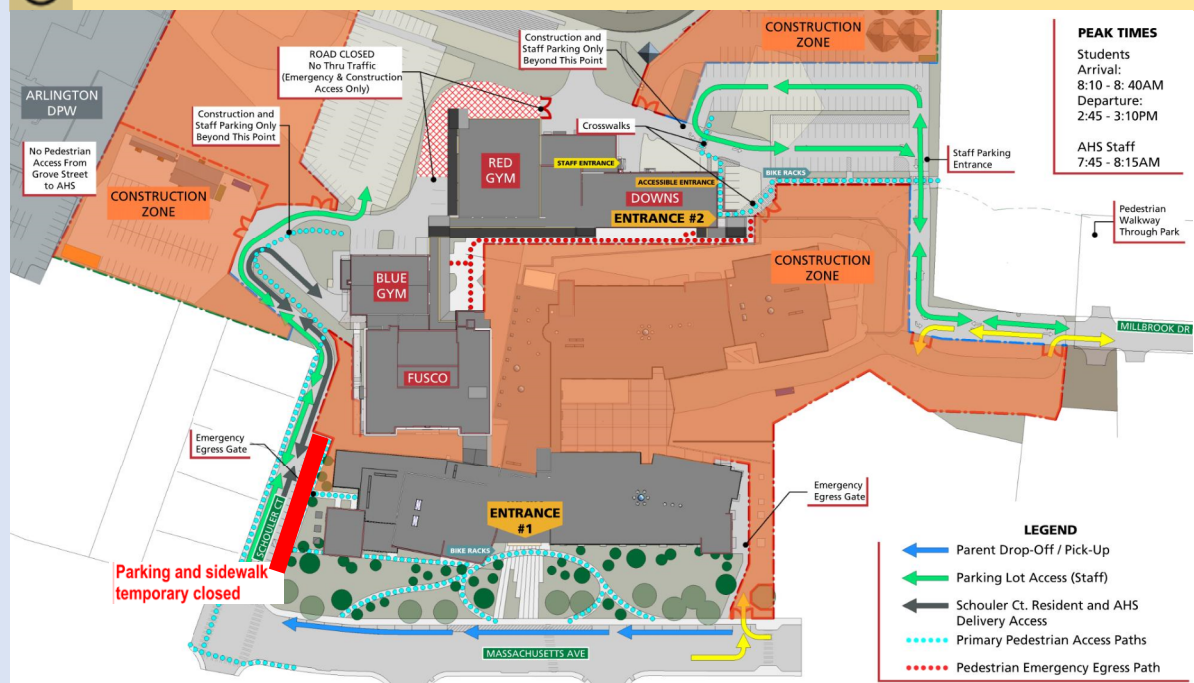

### Construction Look Ahead – Week of August 22<sup>nd</sup>, 2022

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

#### Public Way Impacts

- Deliveries/demo debris trucking ongoing
- Mass Ave access to Main Entrance #1 now open
- Schouler Court sidewalk and parking temporarily offline due to sidewalk improvements

#### General Site Activities:

- Phase 2:
  - Pressure injected footings
  - Debris trucking thru Mill Brook Drive
- Phase 1 Building Closeout:
  - Auditorium finishes
  - Exterior paving and landscaping improvements
  - Chain link fence removal and temporary rope fence installation
- West Parking Lot (adjacent to DPW):
  - Construction trailers and contractor parking
- Material Stockpile/Temp Construction Lot:
  - Contractor storage and parking
- Schouler Court:
  - Construction vehicles entering and exiting project site
  - Sidewalk grading and concrete pouring

#### Weekend Work/Holiday Work/Night Work:

- Saturday work is required for the foreseeable future



Skanska USA Inc.  
Owner's Project Manager



Consigli Construction Co., Inc.  
Construction Manager at Risk



HMFH Architects, Inc.  
Architect





CONSIGLI  
*Est. 1905*

## ARLINGTON HIGH SCHOOL

### WEEKLY UPDATE – WEEK OF AUGUST 22<sup>ND</sup>, 2022

#### Progress Photographs – Taken Week of 8/15/2022



*Photograph 1: Phase 2 Foundations Progress*



*Photograph 1: Building D/E South Elevation (Main Entrance #1)*





CONSIGLI  
*Est. 1905*

## ARLINGTON HIGH SCHOOL

### WEEKLY UPDATE – WEEK OF AUGUST 22<sup>ND</sup>, 2022



*Photograph 2: Building E West Elevation (Schouler Court)*



*Photograph 3: D Building Southeast Elevation (Mass Ave)*
